


Technology Services Quarterly Update




★ A GREAT AMERICAN STORY ★

Tech Services Project Update

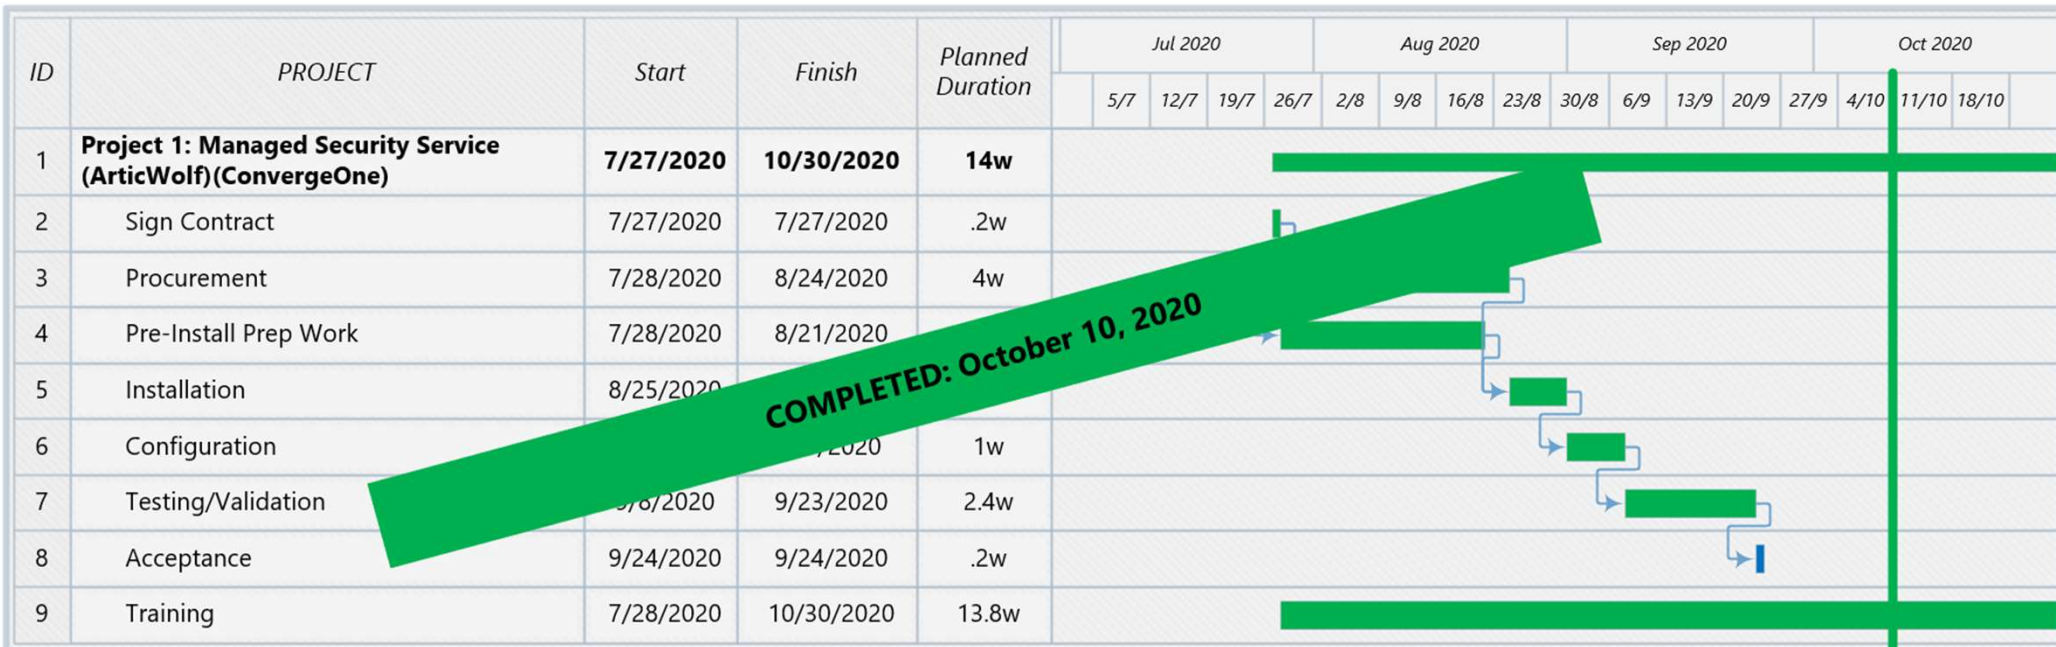

**Actual Completion: Oct 10
(Scheduled -2 weeks)**


Tech Services Project Update

PROJECT	ID	Start	Finish	Planned Duration	Q3 20			Q4 20			Q1 21		
					Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar
Project 2: Security Infrastructure (CheckPoint Infinity)(ConvergeOne)	1	7/27/2020	4/1/2021	35.8w									
Sign Contract	2	7/27/2020	7/27/2020	.2w									
Procurement	3	7/28/2020	8/28/2020	4.8w									
Pre-Install Prep Work	4	7/28/2020	8/28/2020	4.8w									
Installation	5	9/25/2020	9/28/2020	.4w									
Configuration	6	9/29/2020	11/30/2020	9w									
Testing/Validation	7	12/1/2020	3/31/2021	17.4w									
Acceptance	8	4/1/2021	4/1/2021	.2w									
Training	9	7/28/2020	3/31/2021	35.4w									

**Original Scheduled Completion:
Nov 30**

**Projected Completion: Mar 31
(Scheduled +4 months)**

Tech Services Project Update

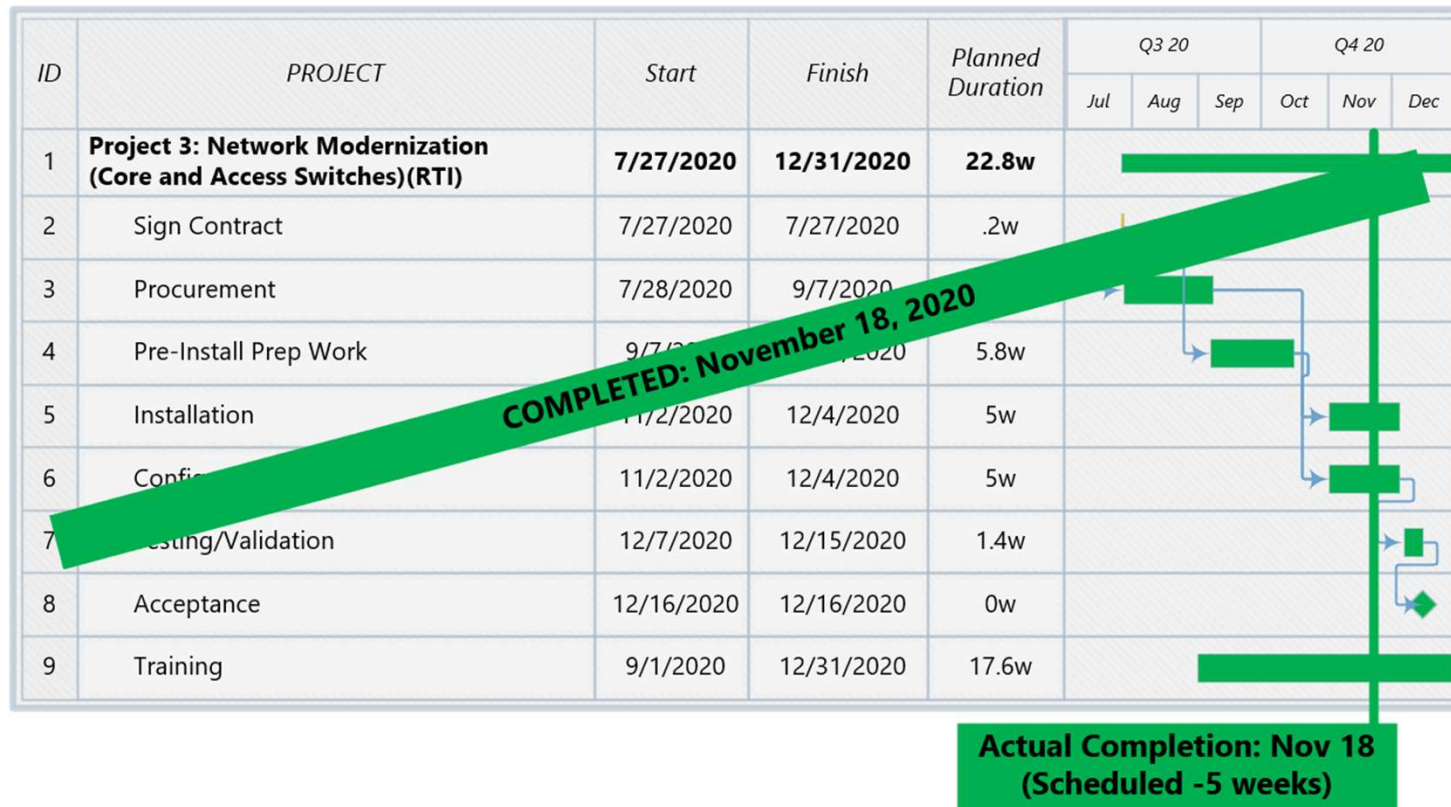

Tech Services Project Update

